

Project Management Plan: QuikFIT Mobile App Development

Mathew J. Bernard

MyPath Department, UMass Global University

CSCC 383: Applied Project Management

Prof. Diana Echols

Feb 14th, 2026

Project Management Plan: QuikFIT Mobile App Development

Introduction

This Project Management Plan outlines the development of the QuikFIT Mobile App, a 20-week project focused on designing, developing, and launching a mobile fitness app that includes guided workouts, instructor-led videos, as well as a user-friendly interface so that users can easily track their progress. The goal of this Project Management Plan is to explain how the project will be carried out, tracked, and managed to make sure all deliverables are finished on time, stay within scope, and remain under the total approved budget of \$220,000. This plan will be the main reference for all project stakeholders throughout the project.

The main goal of the project is to create a fully functioning mobile app that will be available to the public through both the Apple and Android app stores. The project includes clearly defined requirements, approved UI/UX designs, a working prototype, completed backend and frontend systems, integrated workout and video content, testing results, and marketing materials for the launch. The project then finishes with the official app launch, followed by a short period to monitor user feedback and make sure the system is running as it should be.

This project plan shows the management approach, milestone structure, baselines, and monitoring methods that will guide the project from start to finish. This Introduction gives a summary, while the following sections provide detailed explanations of scope, scheduling, cost control, quality standards, communication practices, and risk management strategies. The QuikFIT project has a set timeline and budget, so the team needs to organize overlapping tasks like development, video production, and marketing preparation carefully. Outlining roles, responsibilities, milestones, and baselines, helps this plan to let everyone know what to expect and provide a framework for making informed decisions throughout the project. Following this

plan will make sure that the team delivers a reliable and high quality fitness app that meets both user needs, and organizational expectations, and goals.

Project Management Approach

The QuikFIT Mobile App Development project will follow a milestone-based management approach that's focus is on teamwork across departments, clear roles, and continuous progress tracking. The project manager is mainly responsible for planning, carrying out, monitoring, and closing the project, and also has authority over day-to-day decisions, task order, and management of resources. The project manager will also act as the primary link between the project team and top stakeholders, making sure communication stays clear and consistent. The project will use a matrix organizational structure, which means team members will report to both their own department and to the project manager for day-to-day project tasks. Backend and frontend developers from the IT team will provide technical support. while UI and UX designers will help with gathering the requirements and design work. Marketing staff will be involved during the launch preparation phase, and video instructors along with editors will help with workout content creation and integration. This structure makes it possible to use the specialized expertise from different areas while still keeping overall decision-making under the project manager.

Decision-making authority is shared across different roles. The project manager can approve small schedule changes and operational adjustments as long as they don't affect the project's scope, budget, or core milestones. Any decisions that have to do with changes to scope, reallocating the budget, or extending milestones has to be approved by the project sponsor. Technical decisions related to system design, integration, and quality standards will rely on input from specialized experts from the team, but they'll still be reviewed by the project manager to make sure that everything stays aligned with the project's goals.

The main resource constraints include a limited number of specialized development staff and a fixed budget that is spread across project milestones. To work within these limits, the project timeline has certain tasks overlap when it's possible and efficient, like simultaneously working on development with video production. Progress will be tracked with regular updates, milestones assessments, and comparisons to the pre-approved project plan. This approach helps to keep the project organized while still allowing for enough flexibility to respond to any risks, constraints, and stakeholder needs throughout the project.

Milestone List

The QuikFIT Mobile App Development project is organized into eight main milestones that represent important stages of progress and help to track performance, while also keeping stakeholders informed. These milestones cover the entire 20-week project and show how different tasks are planned and overlap.


M1: Kickoff and Onboarding (Weeks 0–2) sets the project foundation through planning, team onboarding, and role assignment. **M2: Requirements and Design (Weeks 2–5)** focuses on gathering functional requirements and developing and refining UI/UX designs. **M3: Prototype Ready (Weeks 5–8)** shows that a working prototype has been finished and includes the main features of the application. **M4: Core Development (Weeks 6–11)** includes backend and frontend development and represents the most **resource-intensive** phase of the project. **M5: Workout and Video Integration (Weeks 5–11)** covers instructor video creation, editing, and integration into the application. **M6: Testing and Quality Assurance (Weeks 11–16)** makes sure that that system functionality, performance, and quality standards are met. **M7: Launch Preparation and Marketing (Weeks 9–17)** includes marketing content development and app

store submission preparation. The final milestone, **M8: Official Launch (Weeks 17–20)**, includes the official release of the application and monitoring of the initial user feedback.

Milestone dates are set based on the approved schedule and are planned in a way that allows some overlap to save time and use resources efficiently. If those dates need to change because of any approved scope adjustments, limited resources, or identified risks, the updates will go through the formal change management process. Any approved changes will then be clearly communicated to the stakeholders so everyone stays informed and on the same page.

Baselines

Figure 1: QuikFIT Project Schedule Baseline (Gantt Chart)

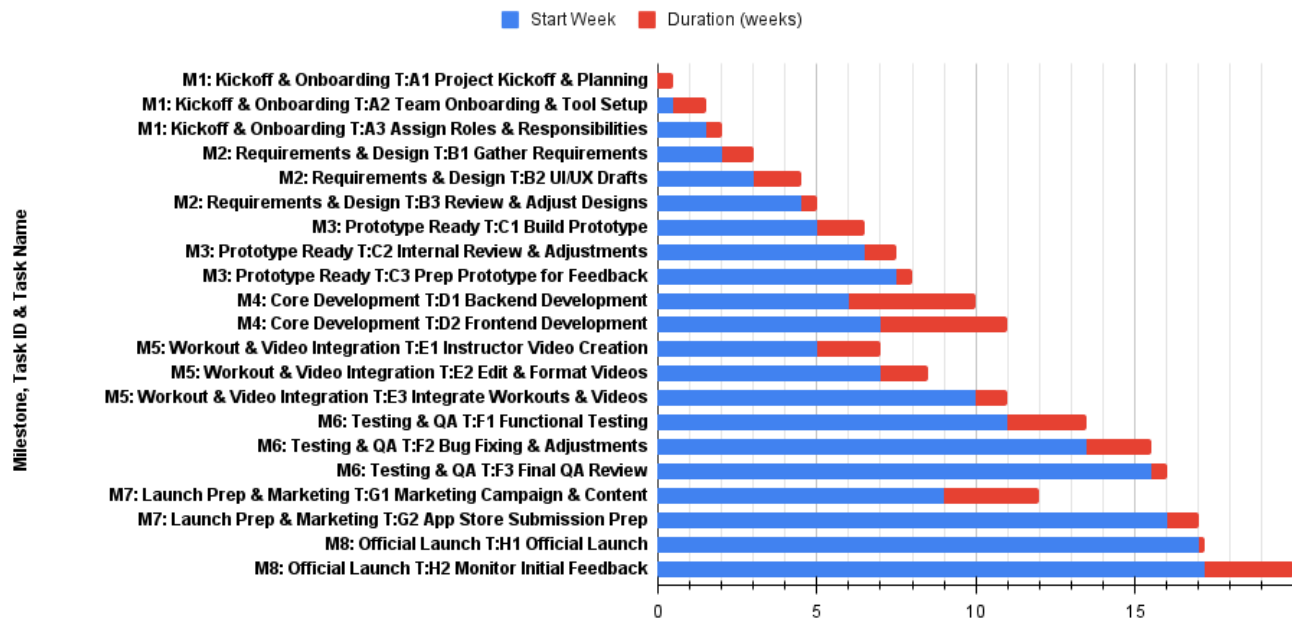

Note: "M" = milestone; "T" = task.

Schedule Baseline

The schedule baseline sets the approved 20-week timeline for the QuikFIT project and acts as the main reference for tracking progress. It's based on the project Gantt chart and PERT dependencies, which outline the order of tasks, how long they take, and where they overlap. Milestones work as checkpoints to measure progress and look for any delays. If the project goes

off schedule, the changes have to be reviewed and approved through the change management process.

Cost Baseline

	Milestone ▲	Budget
1	M1: Kickoff & Onboarding	\$15,000
2	M2: Requirements & Design	\$25,000
3	M3: Prototype Ready	\$30,000
4	M4: Core Development	\$65,000
5	M5: Workout & Video Integration	\$45,000
6	M6: Testing & QA	\$20,000
7	M7: Launch Prep & Marketing	\$15,000
8	M8: Official Launch	\$5,000
9	Total	\$220,000

Table 1: Budget Allocation

The cost baseline outlines the approved project budget of \$220,000 and shows how that amount is divided across the different milestones. It works as a guide for tracking and managing project expenses throughout the process. Cost performance will be monitored by comparing what was planned to what's actually being spent. If spending goes past the acceptable limits, the project manager will need to review the issue and bring it to the project sponsor's attention if necessary.


Scope and Quality Baseline

The scope and quality baseline outlines what the project is expected to deliver, along with the standards those deliverables need to meet. Main deliverables include a functional fitness mobile application with integrated workout videos, a user-friendly interface, backend infrastructure, and completed testing results. Quality standards require that the application runs without major problems, loads content quickly, and reflects the design that was approved during

the prototype phase. This baseline makes sure that the work being done matches the requirements and that the final result is usable and meets the acceptable performance expectations. It also acts as a reference point for checking completed work and helps to maintain consistent quality throughout the project.

Project Scope and Work Breakdown Structure (WBS)

Figure 2: Work Breakdown Structure (WBS)

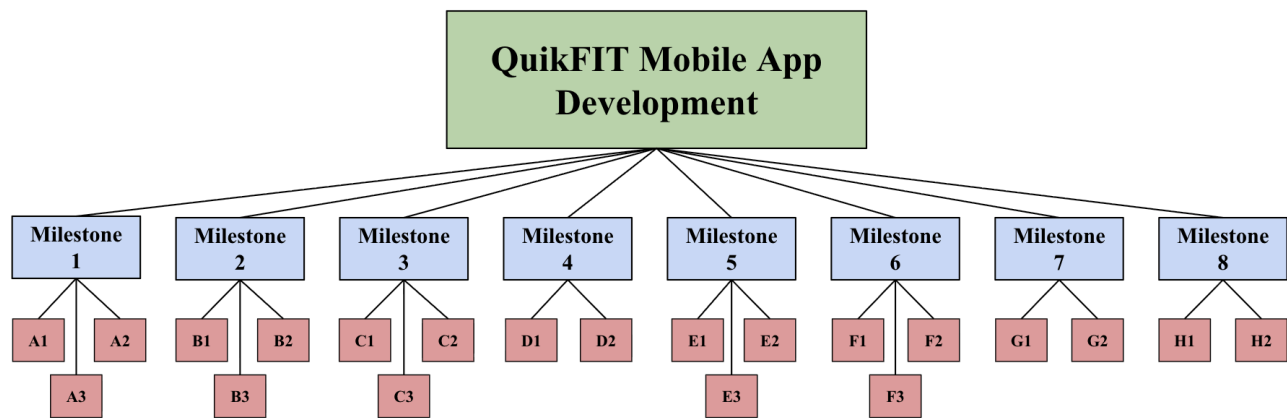

The scope of the QuikFIT Mobile App Development project includes all the work needed to design, build, test, and launch a fully functional mobile fitness app within 20 weeks and a budget of \$220,000. The main goal of this project is to create an app that allows users to watch instructor-led videos, track their diet and fitness progress, and use a clean, easy-to-navigate interface. The scope also covers the planning, design, development, testing, marketing preparation, and post-launch monitoring to make sure the app's release is successful.

The project scope includes the kickoff and onboarding process, gathering requirements, designing the UI and UX, developing a prototype, and completing both backend and frontend development. It also covers creating instructed workout videos, integrating workouts and video content into the app, performing testing for functionality, completing quality assurance checks,

preparing for marketing, app-store submission, and monitoring performance after launch. In addition, the project involves internal reviews, collecting feedback, and fixing bugs to make sure the app meets quality and performance expectations. The project scope excludes long-term app maintenance past the initial monitoring period after launch, ongoing content creation once the app is live, customer support services, or future feature expansions/additions that weren't part of the original requirements. If additional features or extended support are requested outside of the current defined milestones, they'll need to be formally approved before moving forward.

The Work Breakdown Structure (WBS), organizes the project into manageable parts that match with the major deliverables. At the top level, the project is divided into eight milestones: M1: Kickoff and Onboarding, M2: Requirements and Design, M3: Prototype Ready, M4: Core Development, M5: Workout and Video Integration, M6: Testing and QA, M7: Launch Preparation and Marketing, and M8: Official Launch. Each milestone is broken down further into specific tasks, like gathering requirements, creating UI designs, developing backend systems, integrating video content, running tests, preparing for launch, etc. This structure gives a clear breakdown of all the work required to complete each milestone and makes sure no deliverables are overlooked. By defining what's included and excluded, the WBS helps to avoid any confusion, supports accountability, and reduces the risk of unplanned changes to the project scope, which all supports a successful project.

Change Management Plan

The Change Management Plan for this project gives a straightforward process for managing any changes to the project's scope, schedule, cost, or quality. Changes are expected in a complex project, and this plan helps to make sure that each proposed change is carefully reviewed before it gets approved to reduce any disruption and risk. All change requests have to be submitted

using the standard change request form. Requests can come from project team members, stakeholders, or sponsors. Each request should explain the proposed change, the reason for it, and any potential impacts on project deliverables. Once a request is submitted, the project manager will log it in the change tracking register and perform an initial review.

A Change Control Board (CCB) will be responsible for reviewing any change requests and deciding whether to approve or reject them. The CCB includes the project sponsor, project manager, and main team members from development and design. Each request is assessed based on its impact on scope, schedule, budget, quality, and risk. Any changes that affect approved baselines or go over the defined budget need the sponsor's approval. Approved changes will be added to the project plan, and any updates to the milestones, timelines, or costs will be shared with all relevant stakeholders. Rejected changes will be documented with the reason for rejection. A change log will be kept throughout the project to keep transparency and track all requests. This approach makes sure that changes are controlled, documented, and support the project's goals. The Change Management Plan protects the project from uncontrolled scope growth, while also allowing any necessary adjustments, by clearly defining who has authority, how changes are submitted, and how they are tracked.

Communications Management Plan

The Communications Management Plan explains how information will be shared during the QuikFIT Mobile App Development project to keep everyone organized, informed, and engaged. Clear communication is very important to make sure the expectations are understood and that any issues are identified and handled promptly. Different roles have different communication needs. The project sponsor needs high-level progress updates and budget summaries, while the project team needs detailed task information, schedules, and technical updates. External

stakeholders, like marketing partners or content creators, need updates on milestones and details that relate to their responsibilities. Important information that will be shared during the project includes project status, milestone progress, schedule updates, budget performance, risks, issues, and approved changes. This information will be shared through weekly team meetings, biweekly status reports, email updates, and project documents on the shared platforms.

The project manager is in charge of making sure that all project communications are accurate and delivered on time. Team leads handle any updates about their specific tasks and report any issues when needed. Important information like milestone approvals or decision changes, will be documented and saved in the project hub. The core project team will meet weekly to review progress and plan upcoming work. Every two weeks, status reports will be shared with the project sponsor and other main stakeholders. Urgent issues will be communicated as they happen. All communication should be clear, respectful, and relevant. By outlining what information is shared, how it is shared, and who is responsible, this plan helps the team to work together smoothly and efficiently, while avoiding any miscommunication throughout the project.

Cost Management Plan

The Cost Management Plan explains how the costs of the project will be estimated, tracked, and controlled throughout the project. The total approved budget is \$220,000, with funds distributed across defined milestones to make it easier to track spending and support accountability. The project manager is in charge of monitoring costs, while any changes to the budget have to be approved by the project sponsor, based on recommendations from the project manager and the Change Control Board. Costs are monitored on a milestone level to give a clear view into spending for each major deliverable.

Cost performance will be tracked by comparing planned costs to actual spending and checking progress at major points throughout the project. This helps the project team to find any differences early on and take action if needed. Acceptable cost variances are set during planning, and any variance that goes over the limits will be reviewed. Cost reports will be created every two weeks and included in project status updates. These reports show budget allocation, what has been spent so far, remaining funds, and anticipated costs. They are shared with the project sponsor and major stakeholders so that everyone can make informed decisions. Any change requests that affect costs have to go through the formal change management process, and approved changes will update the cost baseline and future reports. Clear responsibilities, defined tracking methods, and consistent reporting practices help the Cost Management Plan to keep the project on budget and in line with organizational expectations.

Procurement Management Plan

The procurement management plan for the QuikFIT Mobile App project explains the steps, responsibilities, and processes needed to obtain the goods, services, and resources that are essential for the project's success. This includes obtaining software licenses, cloud hosting services, development tools, marketing materials, video production equipment, and any outside contractor support needed for app design, testing, and the official launch. The project manager is in charge of overlooking all procurement activities and works closely with the project team, the contracts and purchasing department, and any third-party suppliers.

Procurement starts by identifying all project requirements that can't be handled internally. A formal request for proposals or quotes is sent to potential vendors, and then the responses are evaluated based on cost, quality, and how quickly they can be delivered. After the vendors are chosen, formal contracts will be set up to clearly define deliverables, timelines, and payment

terms. The project manager can approve procurement decisions as long as they stay within the budget, however, any changes outside the budget must be reviewed and approved by the project sponsor. Every step of the process, from the initial request to the completion of the contract, will be tracked using project management software to monitor vendor performance, delivery schedules, and costs. Regular progress reviews will make sure that everything stays on schedule and meets the project milestones. Following a clear procurement process helps the project team to make sure resources are obtained efficiently, maintain quality, and reduce risks of any delays or low quality vendor performance.

Project Scope Management Plan

The project scope management plan explains how the project's scope will be created, tracked, and controlled to make sure it's completed successfully. The project manager is primarily responsible for managing the scope, with support from the development team, UI/UX designers, and major stakeholders. The scope starts with the project charter and is then expanded into a work breakdown structure (WBS) that clearly lays out all deliverables and tasks.

The project scope covers designing, developing, and launching a fully functional mobile app for fitness tracking, workout programs, and video integration. Important deliverables include backend and frontend development, creating instructor videos, functional testing, preparing marketing materials, and official launch of the app. Items that are excluded in the scope are ongoing app maintenance after the official post launch monitoring, customer support services, and new app features that weren't part of the original plan. The scope will be assessed through detailed quality checklists, reviewing work packages based on the WBS, and regular milestone assessments. The scope baseline will work as a guide for all project activities, helping to find any deviations. Any suggested changes to the scope have to be sent to the project manager, then be

reviewed for their impact on budget, schedule, and resources, and lastly will need approval from the project sponsor before moving forward.

Final approval of the project deliverables is the responsibility of the project sponsor, who is responsible for confirming that all tasks listed in the WBS and project plan matches with the required quality standards. The scope management plan helps to keep expectations clear for the project team, avoids any unnecessary work, and lowers the chances of delays, added costs, or unfulfilled stakeholder needs. Clearly outlining roles, processes, and review methods will make sure the plan supports consistent alignment with project goals throughout the entire project.

Schedule Management Plan


The schedule management plan explains how the QuikFIT Mobile App project timeline will be created, tracked, and managed to support on time completion. The project manager will overlook the overall schedule, while team leads will be responsible for monitoring progress within their assigned tasks. Tools like Microsoft Project and Gantt charts will be used to build, update, and share the project schedule, including task lengths, dependencies, and important milestones. Major milestones for the project include the initial kickoff, finishing requirements and design, preparing the prototype, completing core development, integrating videos, performing testing and quality assurance, preparing for the official launch, and then finishing with the official launch. Each task has a clear start and end week, and dependencies are shown in the PERT chart to keep the workflow organized and on track. Resources are allocated carefully to prevent overlaps, making sure that the development, testing, and marketing efforts are supported properly throughout the project.

Schedule performance will be tracked by comparing planned start and finish dates to the actual progress, tracking milestone completion, and reviewing the predetermined track. If the

project starts to fall behind schedule, the team will need to review what had caused the delay and decide what adjustments are necessary for getting the project back on track. Progress updates will be shared weekly with the project team and stakeholders through status reports and meetings. Following this schedule management plan will help to keep tasks organized, use resources efficiently, and finish the project on time.

PERT Chart Development

Figure 3: QuikFIT Project Dependency Diagram (PERT Chart)

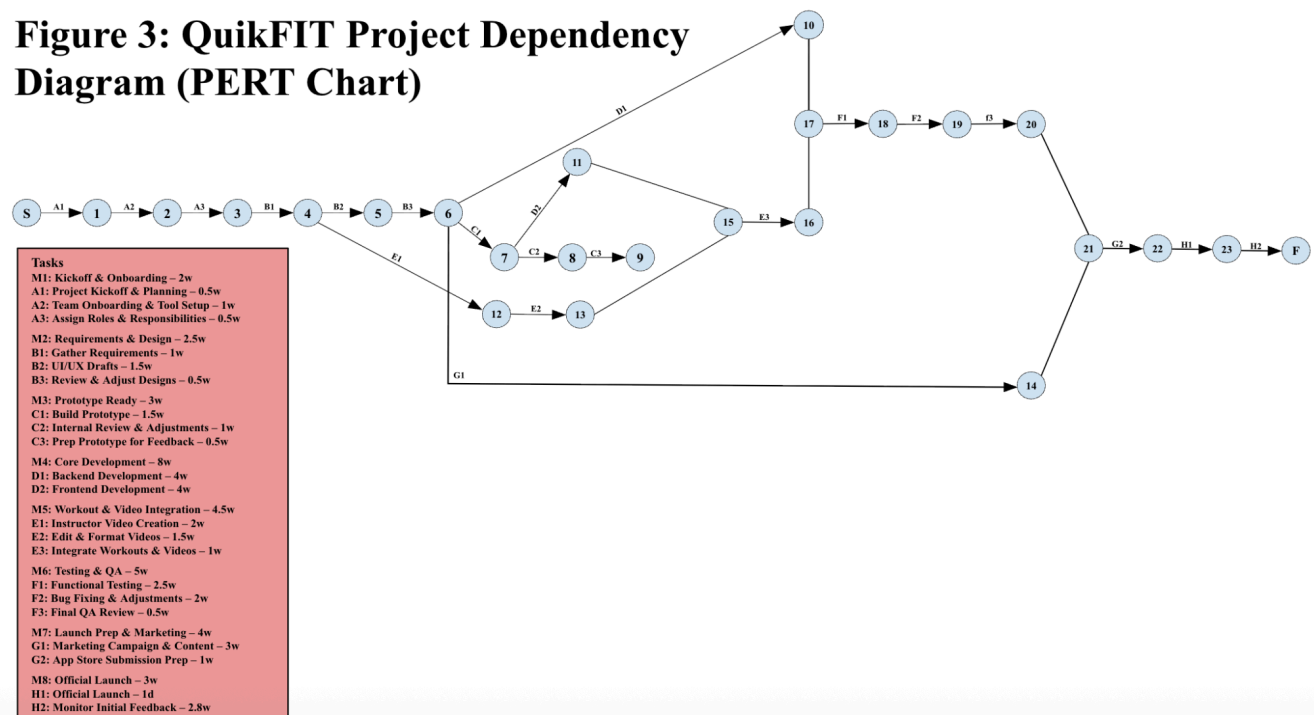

The Program Evaluation and Review Technique (PERT), was used to show how tasks are connected in the QuikFIT Mobile App project. The PERT chart is set up as a precedence diagram, where arrows represent individual tasks and nodes show completion points. The chart starts with the project kickoff (A1) and moves through the main sequence of tasks (A2, A3, B1, B2, and B3) before splitting into multiple paths. At node 6, the work branches into three parallel tracks: prototype development (C1, C2, and C3), backend development (D1), and early marketing efforts (G1). Video production tasks (E1 and E2) branch off earlier from node 4.

Important merge points happen when multiple tasks come together and have to be completed before the next step can start. For example, Circle 15 requires both the frontend work (D2) and the edited videos (E2) to be finished before integration (E3) can move forward. Circle 17 needs the backend development (D1) and integration (E3) to be completed before testing (F1) can start. Similarly, Circle 21 needs both QA approval (F3) and marketing tasks (G1) to be finished before preparing for the app's submission (G2). The PERT chart clearly shows the project's path, which follows the main sequence from development through testing and into the official launch. It also helps to see where the schedule has flexibility and where delays could have the biggest impact to the final completion date. The chart is included as Figure 3, with a text box that explains all task codes.

Quality Management Plan

The Quality Management Plan for the project defines the standards and processes needed to make sure that all the deliverables meet the required standards. The project manager overlooks the overall quality, while each team lead has the responsibility of maintaining quality within their own respective area. The main quality goals for this project are making sure the app works reliably, workout content is accurate, and easy to follow, the interface is easy to use, and that all parts are delivered on time. Quality responsibilities are assigned across the teams. The backend and frontend development teams will focus on following coding standards, making sure it functions smoothly, while system integration is supported. The UI and UX team has the responsibility of consistency in the design, accessibility, and the overall user experience. The video production team makes sure that the instructional content is clear and high quality, while the testing team handles functional and regression testing, identifies issues, and confirms that any corrections work as they're intended to.

Quality control includes regular reviews, inspections, and checks to make sure that the deliverables are as expected. Quality assurance makes sure the process is monitored, making sure that development, design, and integration match the predetermined guidelines. QA tasks include milestone reviews, peer code reviews, and internal prototype testing. Quality is continuously monitored through checklists, tracking measures, and milestone assessments. Regular quality audits are also performed to make sure the project standards are being followed. If issues or inconsistencies come up, they are documented and addressed, and notes are documented to help improve future work. Following this Quality Management Plan will make the project have less risk of low-quality work, stay in line with stakeholder expectations, and support the delivery of a dependable and functional QuikFIT Mobile App.

Risk Management Plan

The QuikFIT Mobile App project will use a structured approach to identify, evaluate, and manage risks throughout the project. Potential risks are grouped into areas like technical, operational, scheduling, financial, and stakeholder concerns. The project manager works closely with team leads to look for any risks through team meetings, reviews of past projects, and input from expert team members.

Each risk that is identified is reviewed for how likely it is to happen, how much impact it could have, and how urgent it is. A risk register is kept to track strategies for reducing or managing these risks. High-priority risks, like development delays, vendor problems, or integration issues, have backup plans that include adjusting schedules, reallocating resources, and having alternative vendors ready. Risks are tracked on an ongoing basis, with weekly status updates during project meetings. Any new risks are assessed right away, and plans are updated as

needed. This approach helps to stop any potential problems early and reduces the chances of extra costs, delays or low quality deliverables.

Stakeholder Management Plan

The stakeholder management plan lists everyone who has an interest in the QuikFIT Mobile App project and explains how their expectations and involvement will be managed. Highly important stakeholders include the project sponsor, development team, UI/UX designers, marketing team, content creators, external vendors, and consumers. Stakeholders are grouped based on their level of influence and interest, which helps to decide how often and how much information they get. High-influence stakeholders, like the project sponsor and senior management, get weekly updates, milestone reviews, and are involved in important decisions. Medium-influence stakeholders, like team leads and vendors, receive progress reports every two weeks, updates on tasks, and notifications about any risks. Low-influence stakeholders, including app testers get occasional updates on the overall progress of the app development and are asked to give suggestions.

The project manager handles all interactions with stakeholders, making sure that any concerns are dealt with promptly and decisions are shared clearly. Communication happens through email, virtual meetings, progress dashboards, and milestone reports. Feedback from stakeholders is gathered and added to the project plan when needed. Maintaining strong relationships with stakeholders keeps the whole team engaged, helps the project stay on track, and helps to avoid any miscommunication or frustration.

Staffing/Human Resource Management Plan

The project will follow a matrix organizational structure, which mixes guidance from core departments with dedicated project teams working on specific tasks. The project manager

organizes resources across development, design, testing, and marketing to make sure that the work is distributed efficiently, and effectively while keeping everyone accountable for their deliverables. Core team members include backend and frontend developers, UI/UX designers, instructional video producers, testers, and marketing specialists. Each person is given specific tasks based on the WBS so that all responsibilities are clear. Project tasks are done by the company staff and, when needed, external contractors for video production or any specialized app features. Contracts clearly show deliverables, timelines, and performance expectations to make sure everything stays on track with the project milestones.

Staff management responsibilities include assigning tasks, monitoring performance, and offering training to strengthen the team's skills where necessary. Regular team meetings and progress evaluations help everyone to stay accountable, work together, and find any resource issues. The matrix structure makes it much easier to move people to the tasks that could need more attention if time becomes limited, which helps to avoid delays. Using this approach makes sure that everyone's time is used effectively, that team members know their responsibilities, and that the QuikFIT Mobile App is finished on time, within budget, while meeting high quality standards.
